


Monthly Target of Excavation (Sept/ 2012)

24/Aug/ 2012

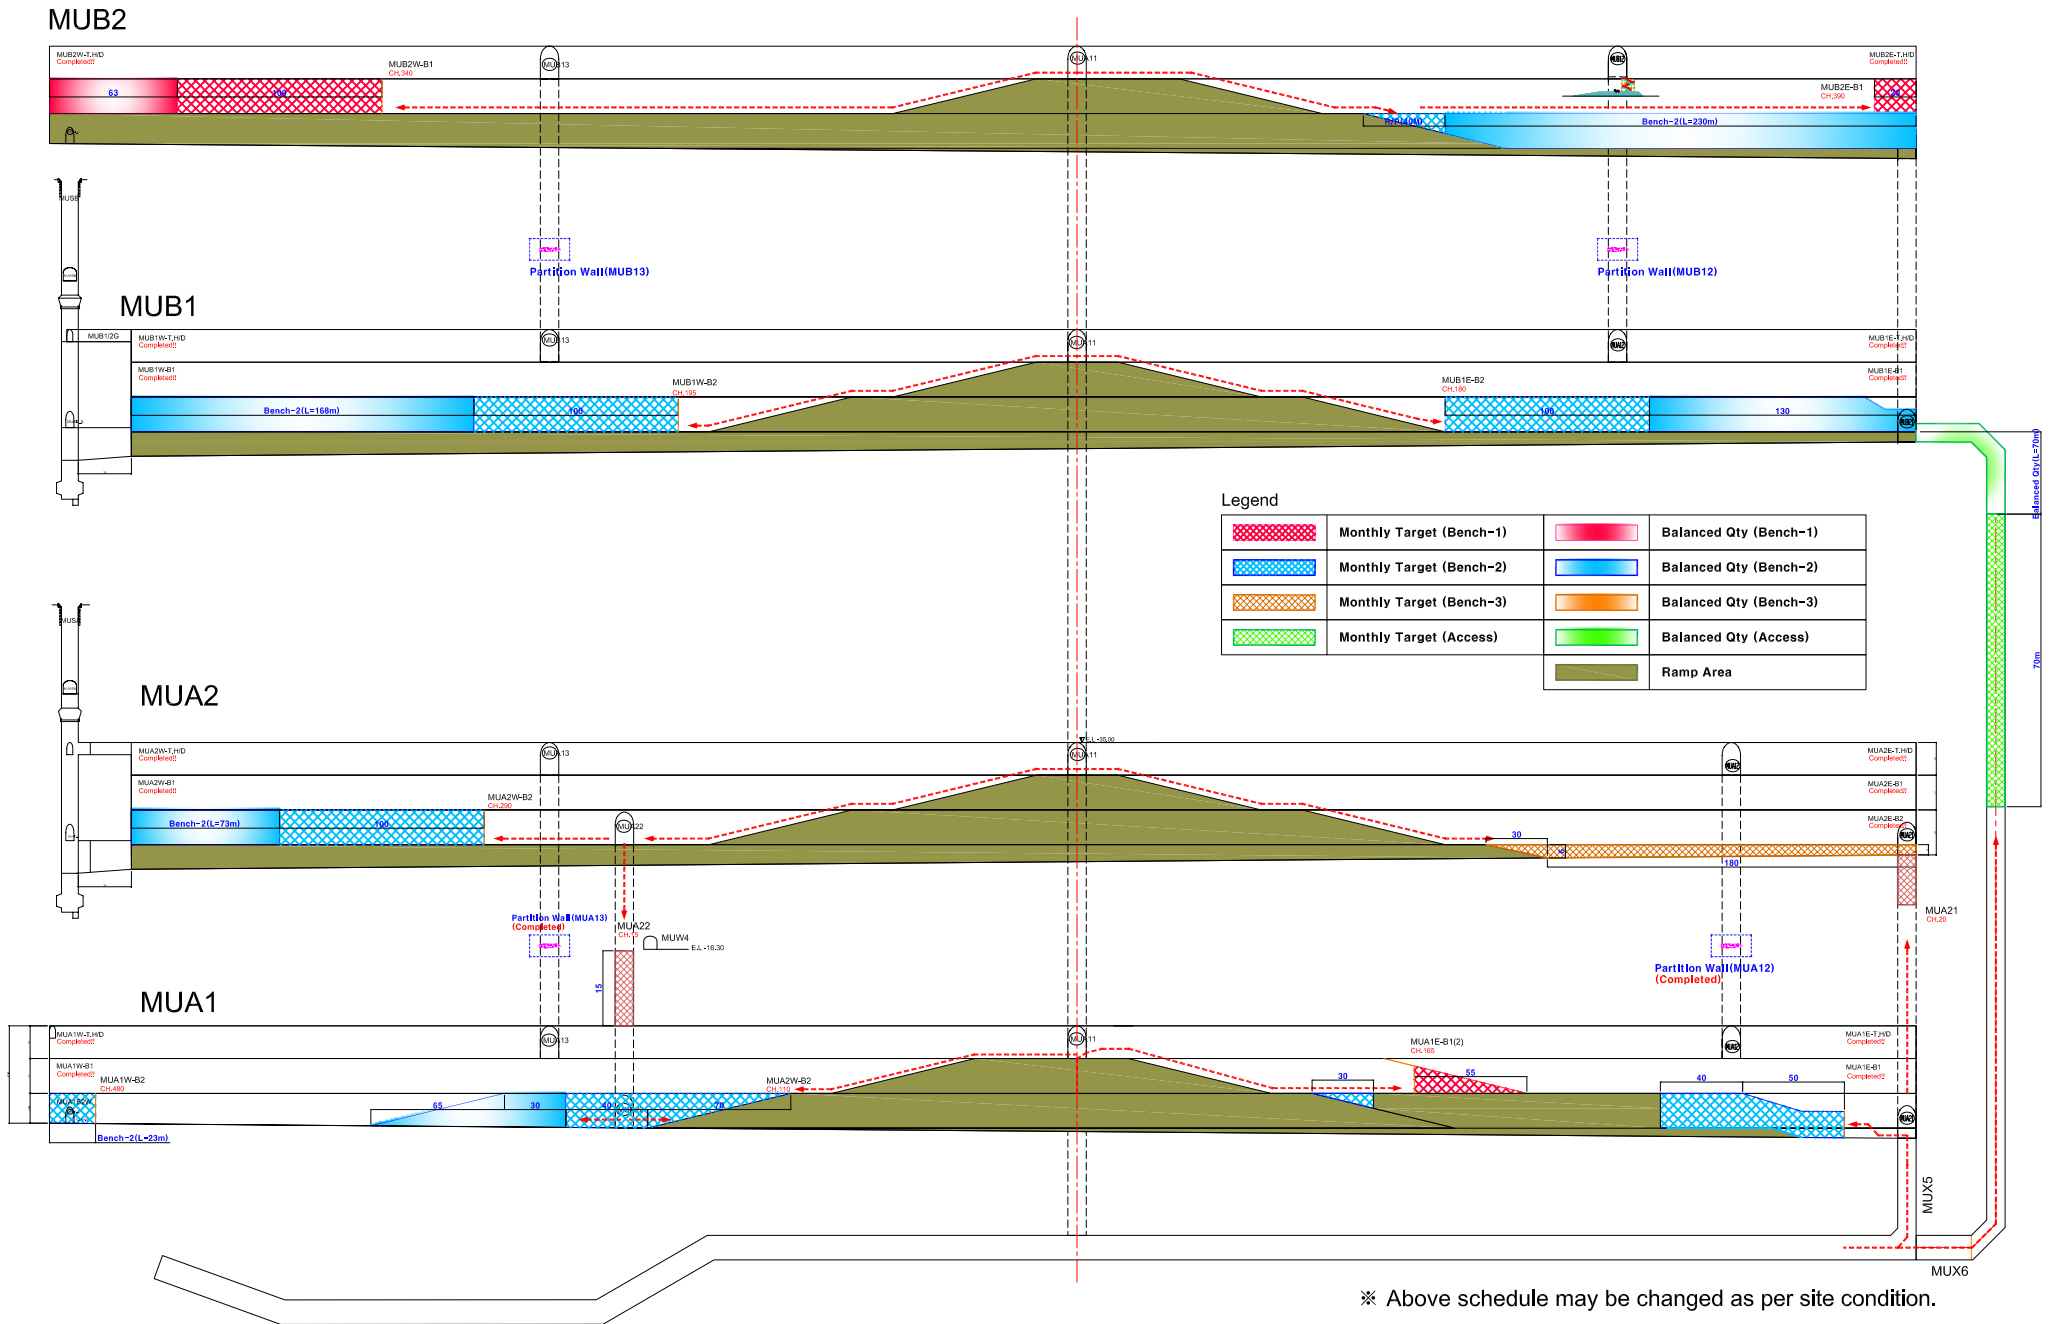

Location			Section (m2)	September-12		Note	
				Target			
				L(m)	V(m³)		
Main Cavern	Bench 1	A1E_B1-R/P(2)	85.0	55.0	4,675.0		
		B2E_B1	170.0	20.0	3,400.0		
		B2W_B1	170.0	100.0	17,000.0		
	Total				175	25,075	
	Bench 2	A1E_B2-R/P(2)	85.0	30.0	2,550.0		
		A1E_B2-R/P-Remv	85.0	50.0	4,250.0	Ramp Remove	
		A1E_B2-Reverse	170.0	40.0	6,800.0	Reverse from X5	
		A1W_B2-R/P	85.0	70.0	5,950.0		
		A1W_B2	158.0	63.0	9,954.0	Section Reduced	
		A2W_B2	170.0	100.0	17,000.0		
		B1E_B2	170.0	100.0	17,000.0		
		B1W_B2	170.0	100.0	17,000.0		
		B2E_B2-R/P	85.0	40.0	3,400.0		
	Total				593	83,904	
	Bench-3	A2E_B3-Ramp	27.5	30.0	825.0		
		A2E-B3	55.0	180.0	9,900.0		
Total				210	10,725		
Sub Total				978	119,704		
Miscellen.	ACT	X7-Enlarge	88.0	70.0	6,160.0		
		MUA21	88.0	15.0	1,320.0		
	CCT	MUA22	65.8	15.0	987.0		
Sub Total				100	8,467		
Grand Total				1,078	128,000		
